


**AGENDA
ITEM**

9



AGENDA STAFF REPORT

DATE: February 6, 2019

TO: Mayor and City Council

APPROVED BY: David B. Dale, City Manager *DB Dale*

PREPARED BY: Lilliana Falomir, Public Works Manager *L Falomir*

SUBJECT: Authorize City Manager to Sign Change Order No. 4 with Pyramid Construction and Aggregate, Inc. in the amount of \$255,250.00 for Cesar Chavez Blvd. Improvements Federal-Aid Project No. HPLUL-5168(017).

=====

Recommendation:

Authorize City Manager to Sign Change Order No. 4 with Pyramid Construction and Aggregate, Inc. in the amount of \$255,250.00 for Cesar Chavez Blvd. Improvements Federal-Aid Project No. HPLUL-5168(017).

Background:

The City of Calexico Public Works Department has received a grant from the Department of Transportation for construction in the amount of \$7,104,240.00 (Federal \$5,500,000.00 and Local Match \$1,604,240.00) for Federal Project No. HPLUL-5168(017) Cesar Chavez Blvd./Calexico-West Port of Entry between HWY 98 and Second Street HPLUL-5168(017) Cesar Chavez Blvd./Calexico-West Point of Entry between HWY 98 and Second Street.

On August 1, 2018 the City Council of the City of Calexico awarded a construction contract to Pyramid Construction and Aggregate, Inc. for the above-mentioned project in the amount of \$6,022,219.00.

Discussion & Analysis:

Due to additional work that was not anticipated during the design phase of said project, Public Work staff is requesting that the City Council of the City of Calexico approve the following change order:

- Drainage Improvements at Pierce Avenue and Cesar Chavez Blvd.
- Install "Welcome to Calexico" street sign on signal light



With Change Order No. 4 the new contract amount will be \$7,030,857.00.

Fiscal Impact:


Federal Grant \$255,250.00

Coordinated With:

Public Works Department.

Attachment(s):

- 1. Change Order No. 4



**CITY OF CALEXICO
PUBLIC WORKS DEPARTMENT
CHANGE ORDER NO. 4**


Name of Project: Cesar Chavez Blvd. Improvements
Federal-Aid Project No. HPLUL-5168(017)
Name of Contractor: Pyramid Construction and Aggregate, Inc.
Date: 02/06/19

#	Description	Price Increase	Price Decrease	Time Extension
1	Drainage Improvements at Pierce Avenue and Cesar Chavez Improvements	\$ 252,600.00		28
2	Install Welcome to Calexico Street Sign on Signal Light	\$ 2,650.00		1
	Sub-Total	\$ 255,250.00		
	Total	\$	255,250.00	
	Contract Amount	\$	6,775,607.00	
	Total Contract Amount (Contract + Change Order No. 4)	\$	7,030,857.00	

David Dale, City Manager
City of Calexico, 608 Heber Avenue, Calexico, California

Sameer Patel, Project Engineer
The Holt Group, Inc., 1601 N. Imperial Avenue, El Centro, California

Archie Abeyta, Project Manager
Pyramid Construction and Aggregate, Inc., 839 Dogwood Road, Heber, California



**PYRAMID
CONSTRUCTION
AND AGGREGATES, INC.**

General Engineering Contractor
State Contractor Lic. No. 866533

January 14, 2019

The Holt Group
1601 N Imperial Ave
El Centro, CA 92243

RFP Drainage Improvements at Pierce and Cesar Chavez

Pyramid proposes the following as per plans provided on 12/28/18

Pipe Installations

Equipment (excavators, compactors, sawcutting, labor, water truck)	\$ 52,500.00
Trucking	\$ 17,800.00
Sand	\$ 35,000.00
Pipe (plastic)	\$ 18,630.00
Survey	\$ 6,900.00
Traffic Control	\$ 6,000.00
Slurry	\$ 9,000.00
Catch Basins (\$10,000 Each)	\$ 20,000.00
Manhole @ Station 12+11.40	\$ 6,000.00
Total	\$171,830.00
Additional 14 Calendar Days	

Retention Basin

Equipment	\$ 24,000.00
Trucking	\$ 15,000.00
Felt	\$ 3,000.00
Rock	\$ 12,270.00
Place (rock-equipment/labor)	\$ 5,000.00
Total	\$ 59,270.00
Additional 7 Calendar Days	

Drywell


Equipment and Labor	\$ 8,000.00
Trucking	\$ 1,000.00
Felt	\$ 1,000.00
Rock	\$ 3,000.00
Drywell Price	\$ 5,500.00
Concrete Apron	\$ 3,000.00

Total \$ 21,500.00
Additional 7 Calendar Days

Total \$252,600.00

Total Extra Calendar Days 28

Archie Abeyta
Project Manager



**PYRAMID
CONSTRUCTION
AND AGGREGATES, INC.**

General Engineering Contractor
State Contractor Lic. No. 866533

839 Dogwood Road, Heber, CA 92249
Office (760) 337-5839 Fax (760) 337-5993
archie@pyramidca.com

REQUEST FOR INFORMATION (RFI) NO. #42 Date 1.23.19

TO: Sameer Project: Cesar Chavez Blvd
Contract No.: _____
Contractor: Pyramid

ITEM DESCRIPTION AND/OR APPARENT DISCREPANCY Line Item

The cost to install a welcome street sign as proposed is \$2650.00 in addition to the cost of the sign.

Additional contract days 1 Day

RESPONSE REQUIRED BY: 1.31.19 IN ORDER TO AVOID DELAY IN IN PROGRESS


Possible Change(s) To: Contract Price: Contract Time: X

CC:

Archie Abeyta -Project Manager

ISNS Type A housing LED Tube Light

Submittal
ISNS

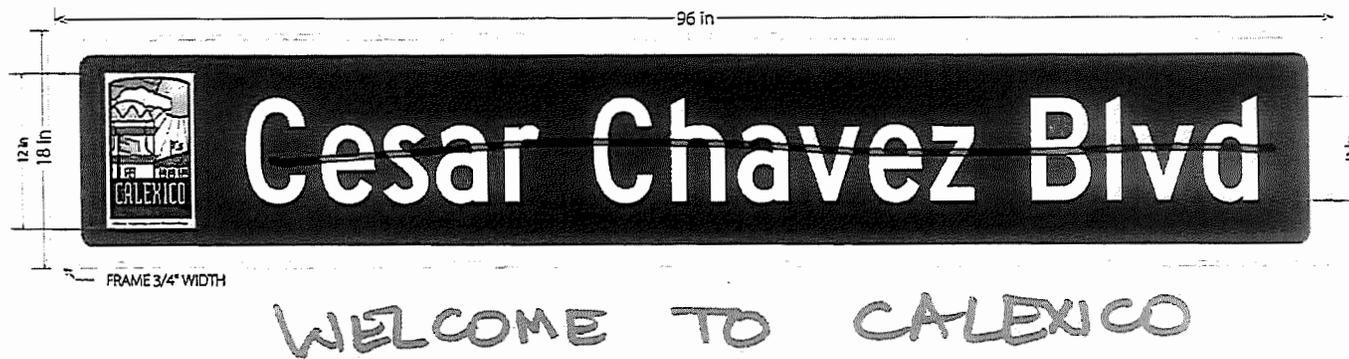

Information

Customer: Perry Electric
PO#: 886
SO#: 4506590
Agency: City of Calexico
Location: N/A
Pole: N/A
Project Mngr: Jesse Phelan

Specifications

ISNS: LED Tube Light, 6'X18" w/Photocell Double/S
Panel: Clear Acrylic 0.125" thick High Impact Modified
Vinyl: 3M 1177 Green on 3M DG 4090 Sheeting
Font: FHWA Series C, 8" UC. & 6" LC.
Border: 1" Radius Border
Logo: 12" Height Decal
Brackets: McCain Clamps & Hanger Set

Created: 10/16/2018

Revised: 12/14/2018

Approved: _____

Date: _____

 McCain

